




The Leadenhall Building 122 Leadenhall Street



British Land

OXFORD

Timeline

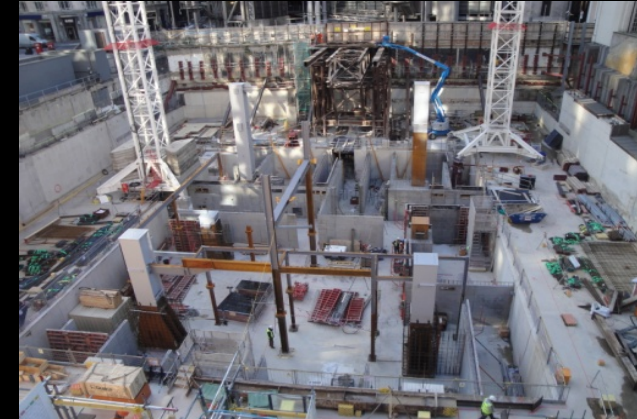

Planning
Consent

Start
Demolition

Project
Suspension

Restart

Joint
Venture

Contract
Placement

Pre-let

Completion

April
2005

March
2007

April
2009

June
2010

December
2010

August
2011




November
2011

Mid
2014




Demolition

- Existing GMW designed building 1969
- Floors suspended from post tensioned structure at roof level
- Demolished from ground up

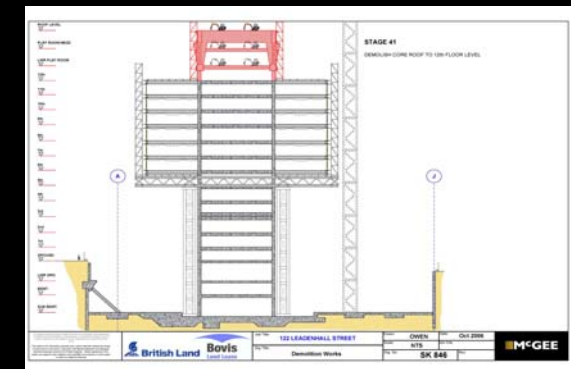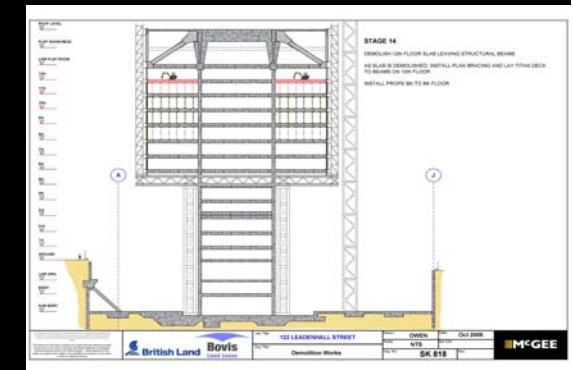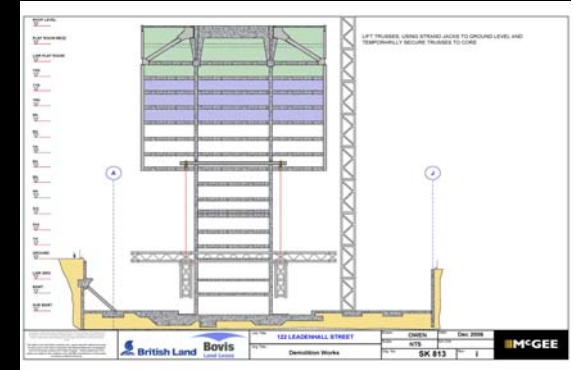

Progress – November 11

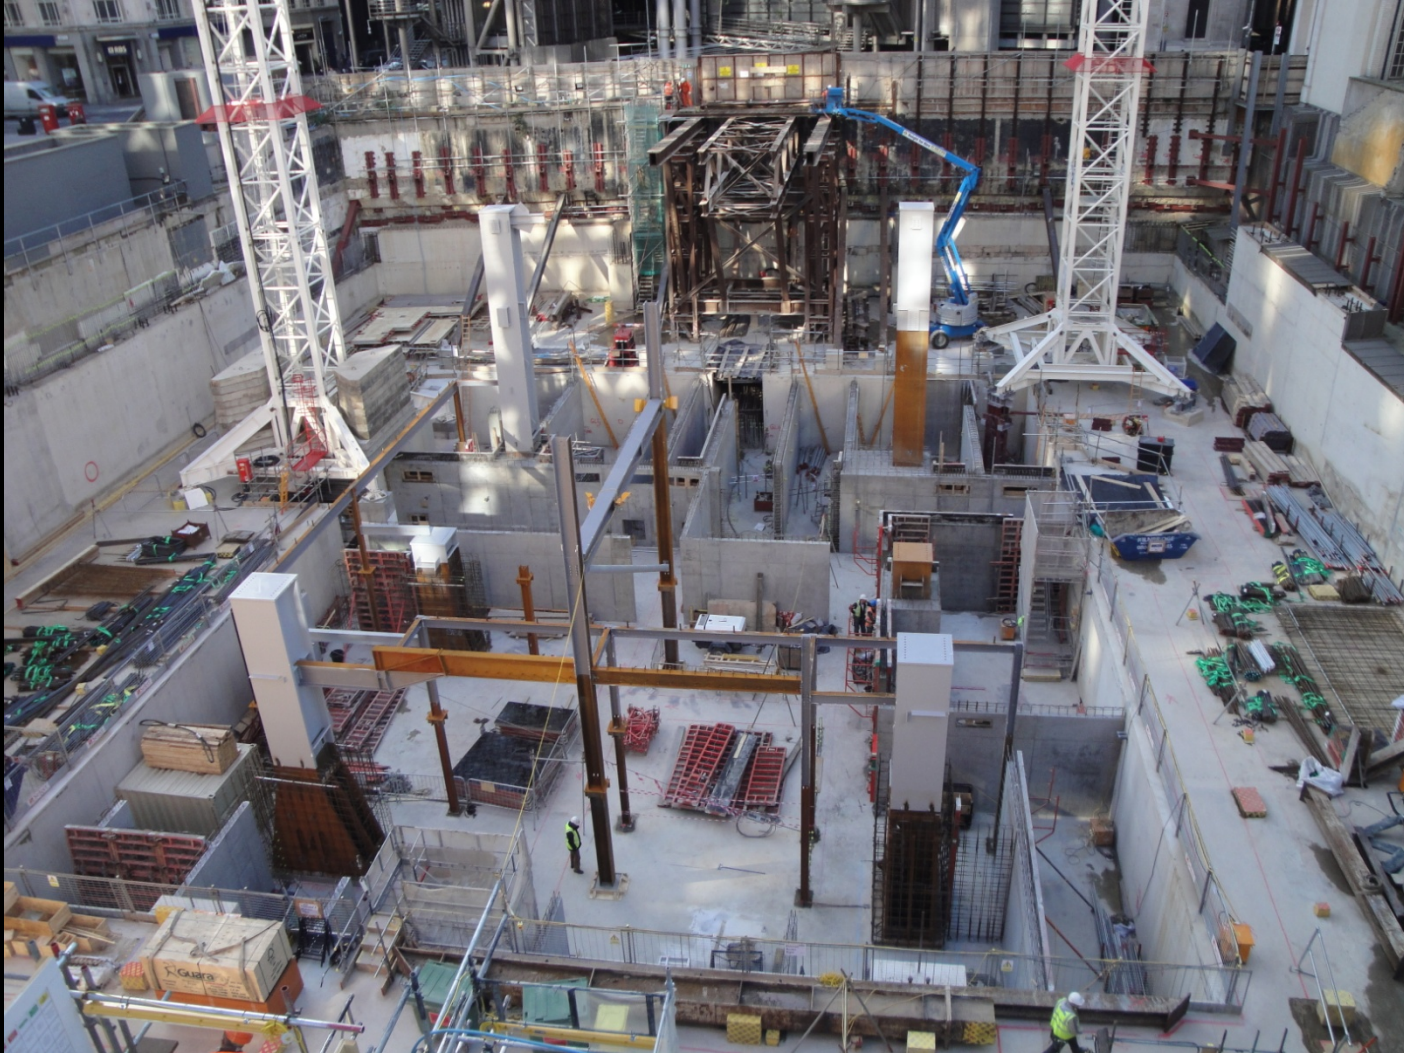

Aon Pre-let

- 191,000 sq ft with further 85,000 sq ft as options
- Levels 4 to 13
- £56-£58 / sq ft
- 19 years average lease term



Space Provided

Total NIA 610,000 Sq ft



Level 45 – 6,000 Sq ft

Level 18 – 16,000 Sq ft

Level 5 – 21,000 Sq ft

Net: Gross


Efficiency above ground 70%

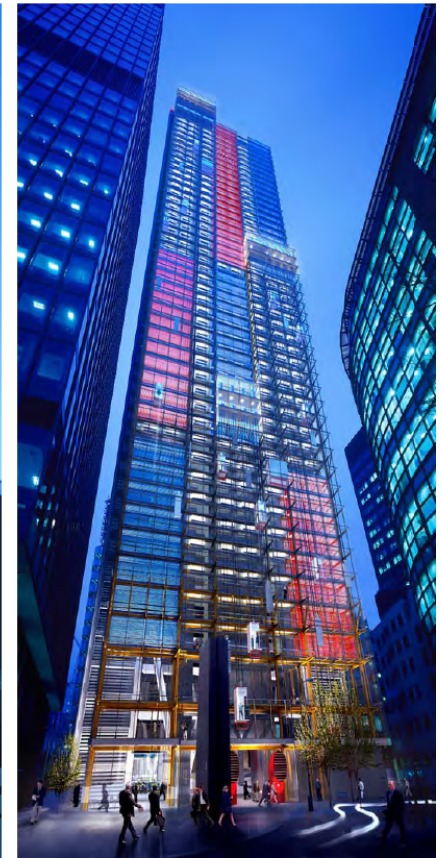





The Leadenhall Building

Rogers Stirk Harbour + Partners

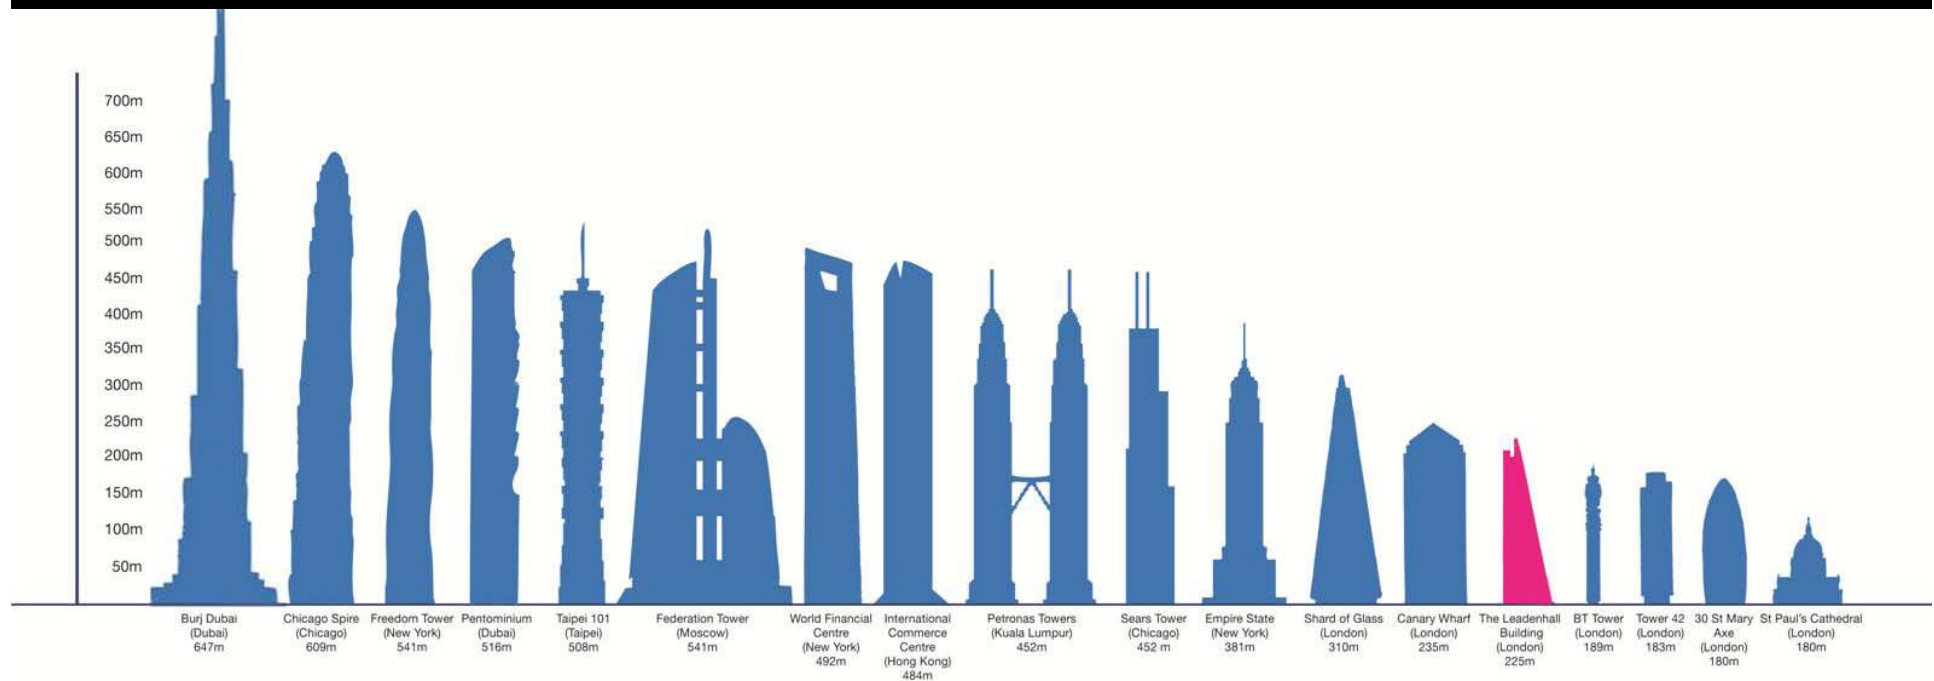



Scale of the building in global context

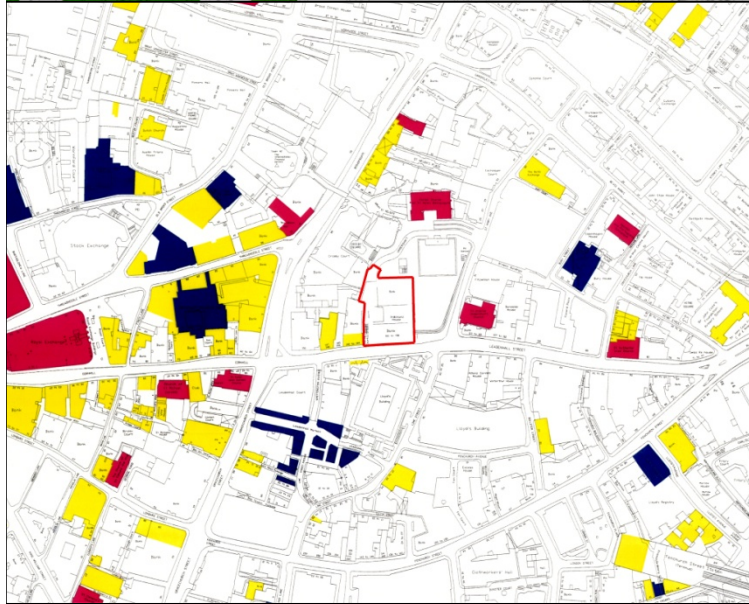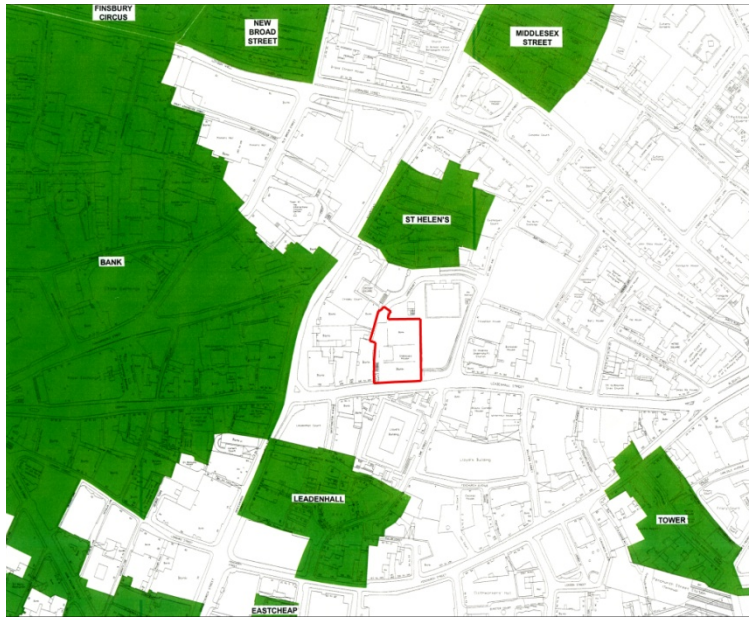





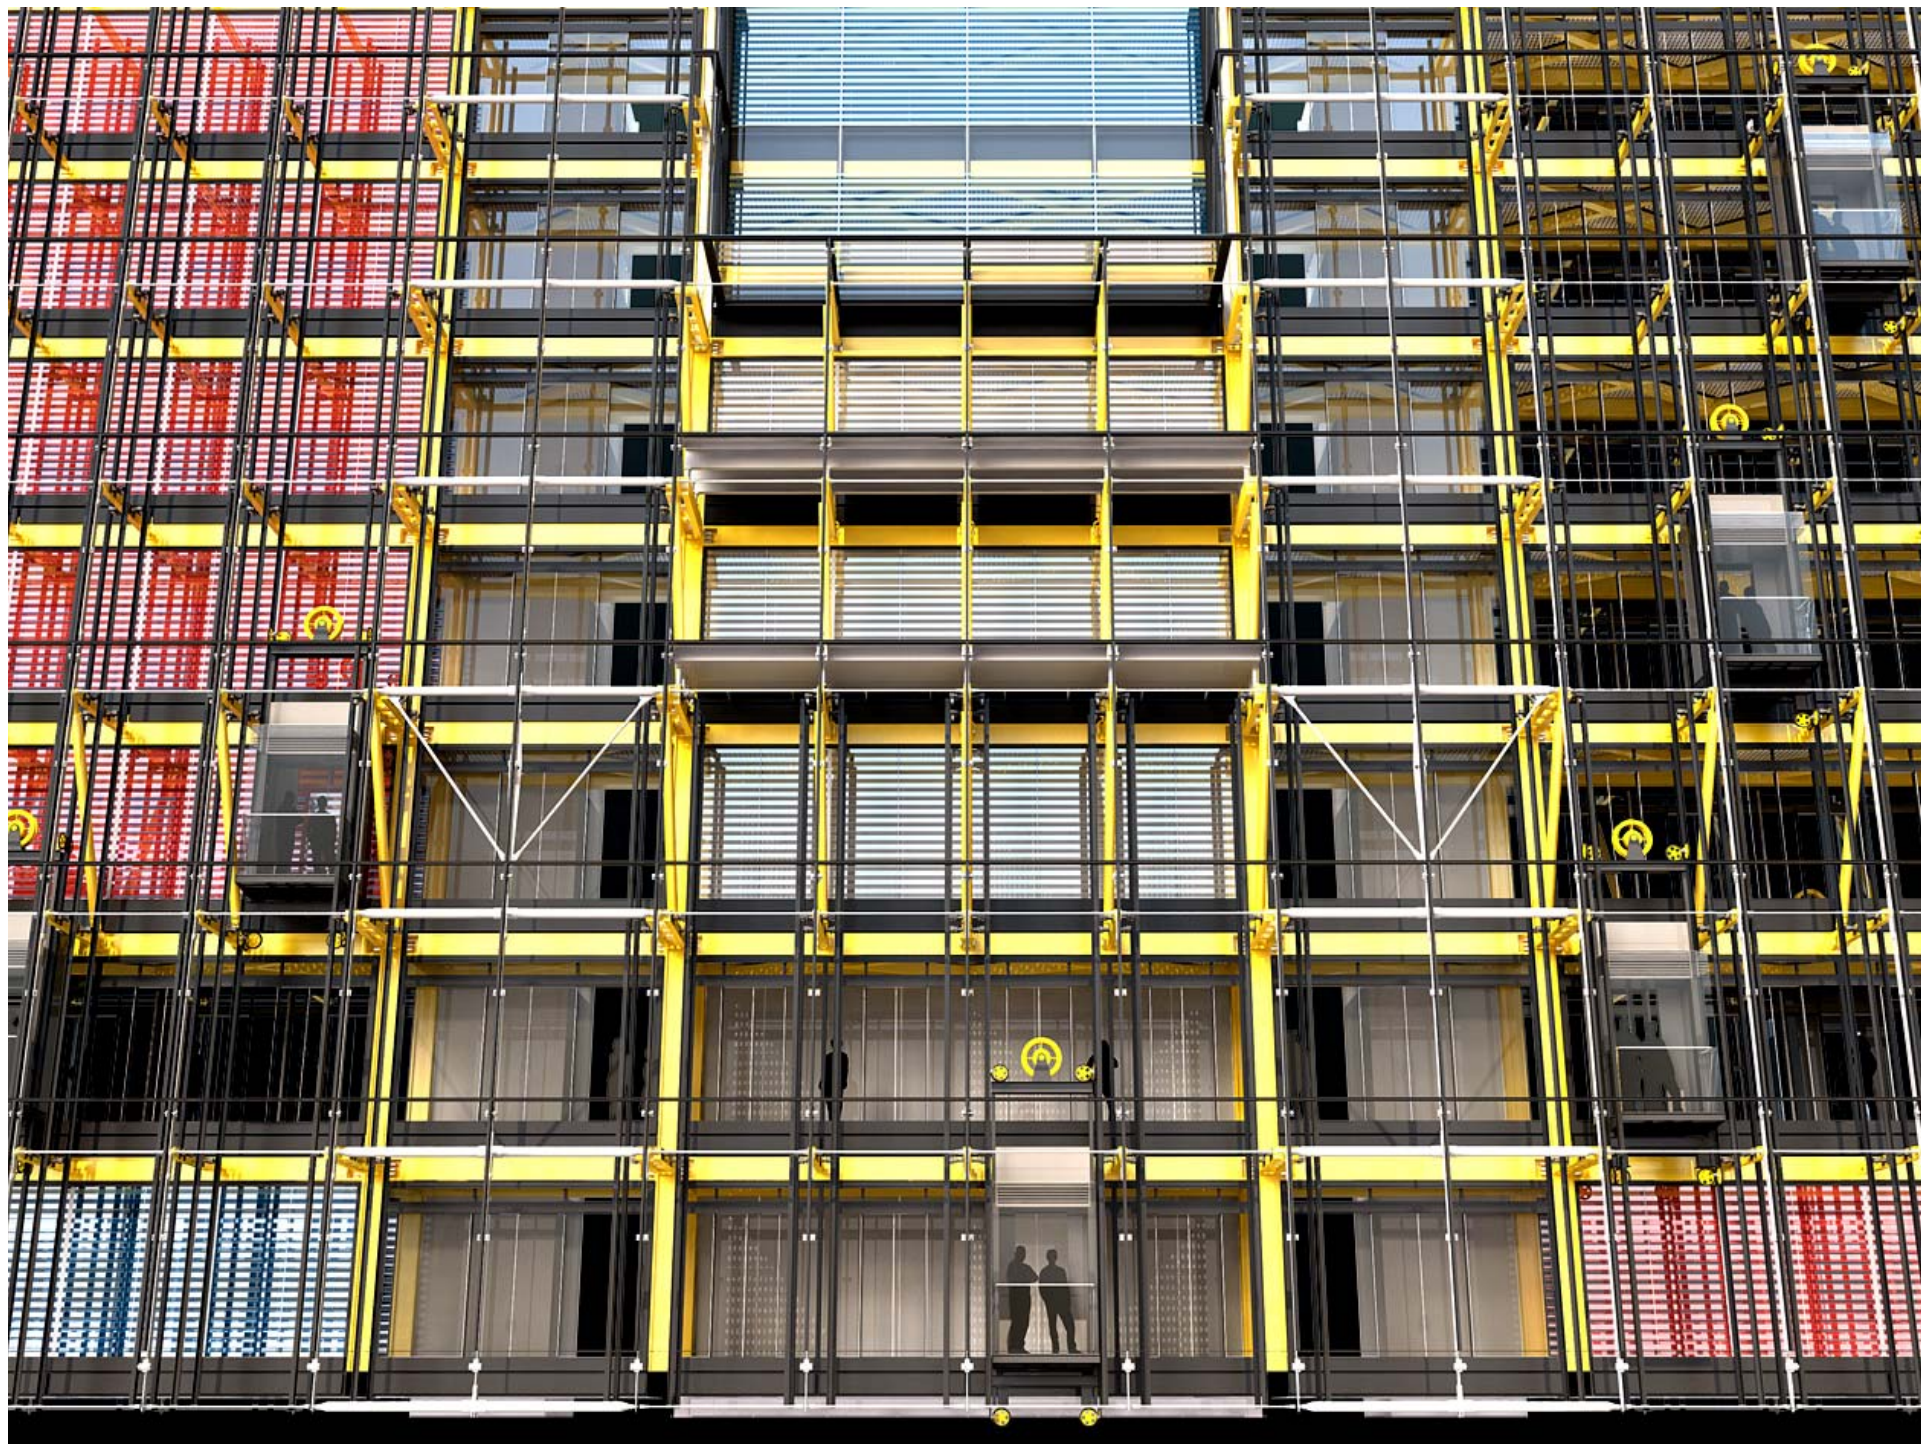


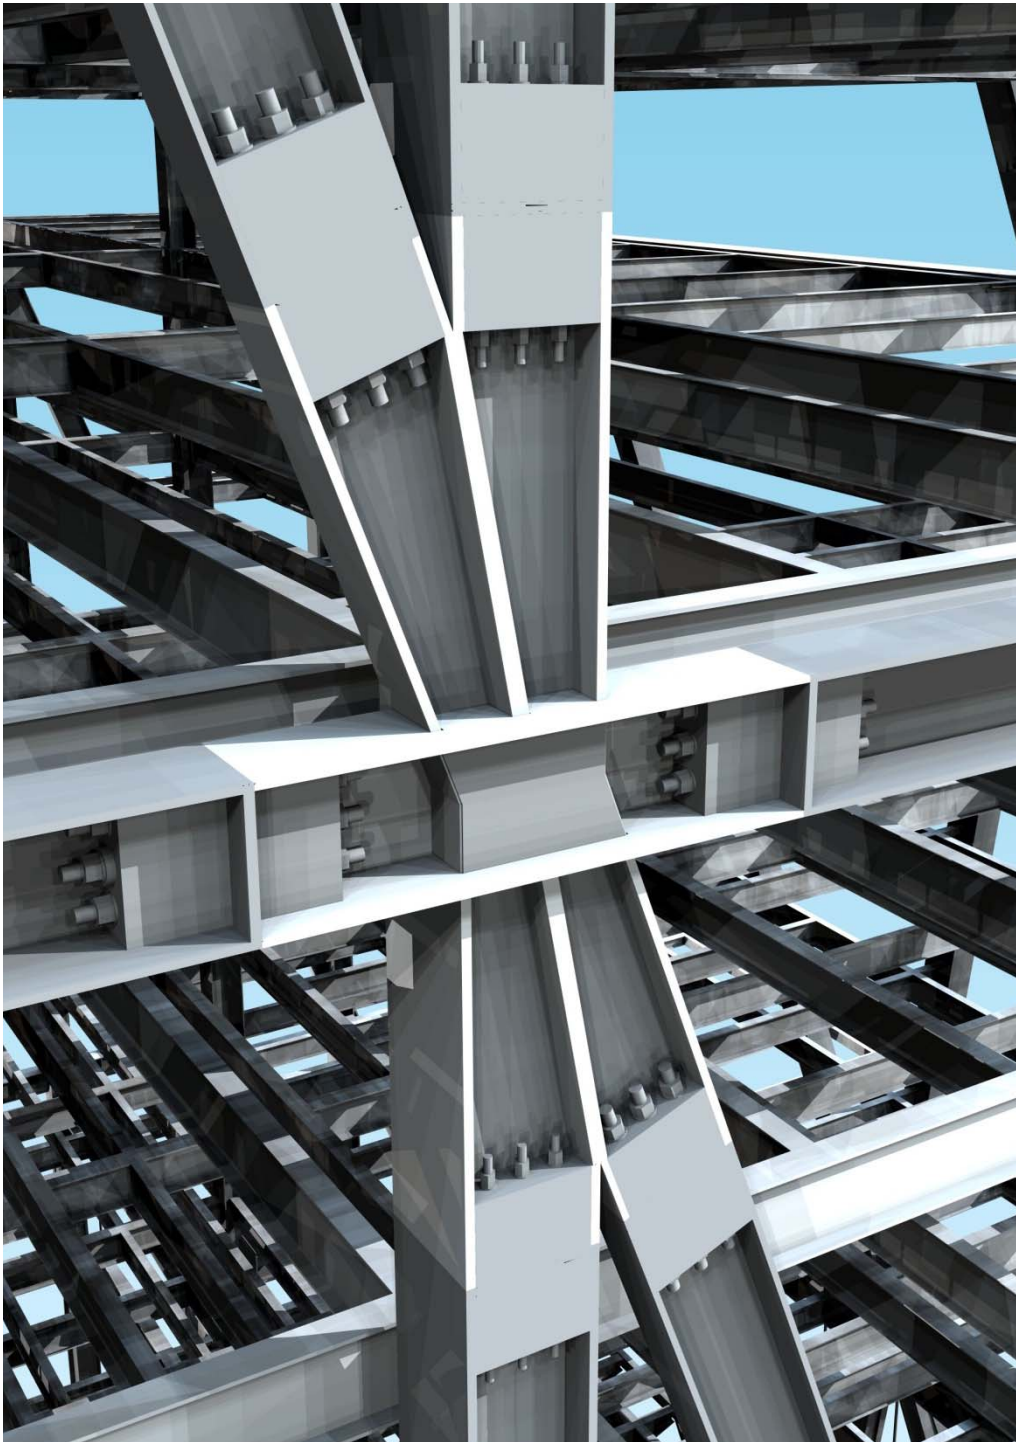


The Leadenhall Building

Megaframe engineering




- Damian Eley

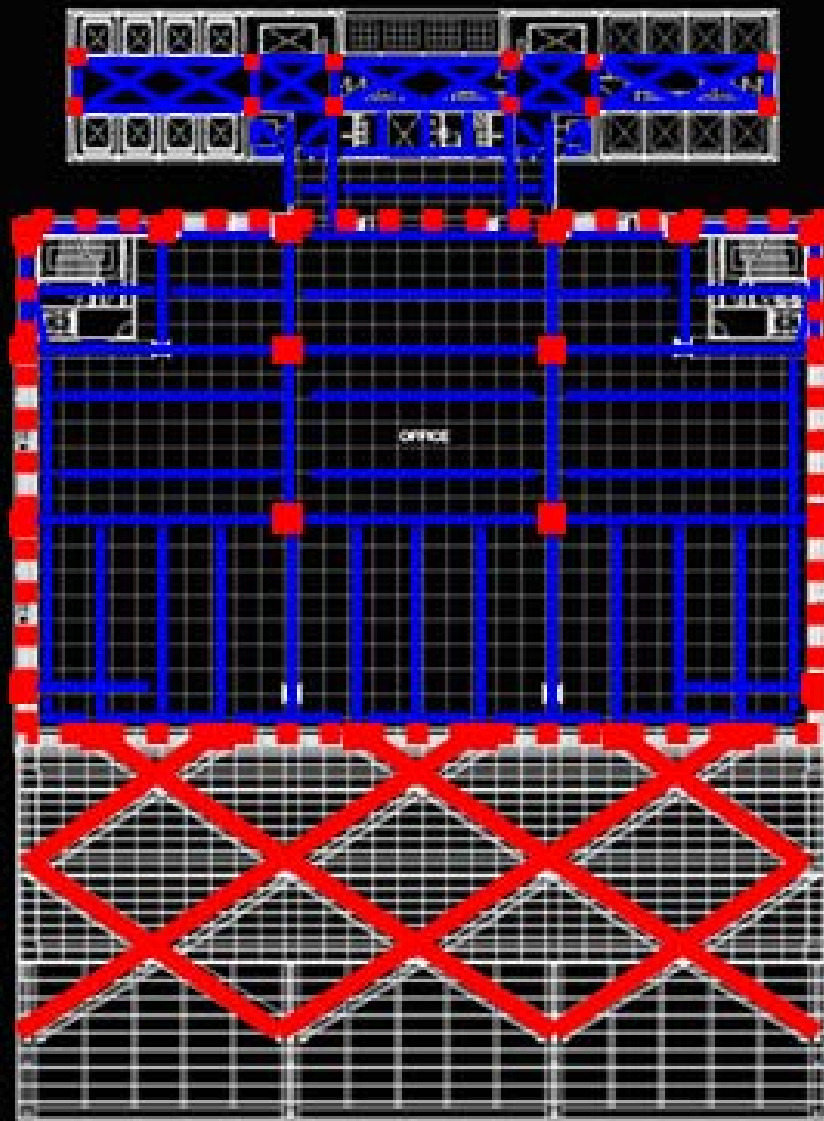

The Megaframe

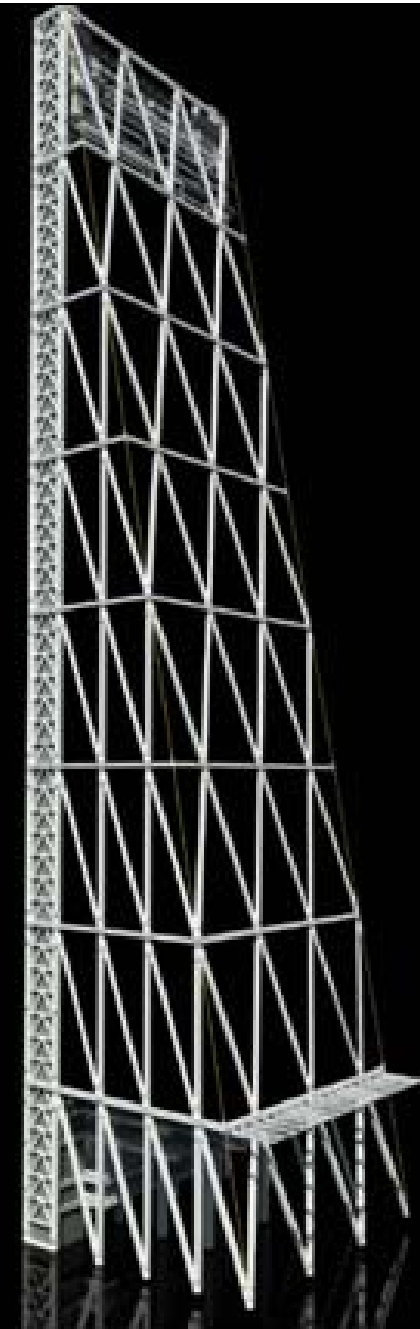


ARUP

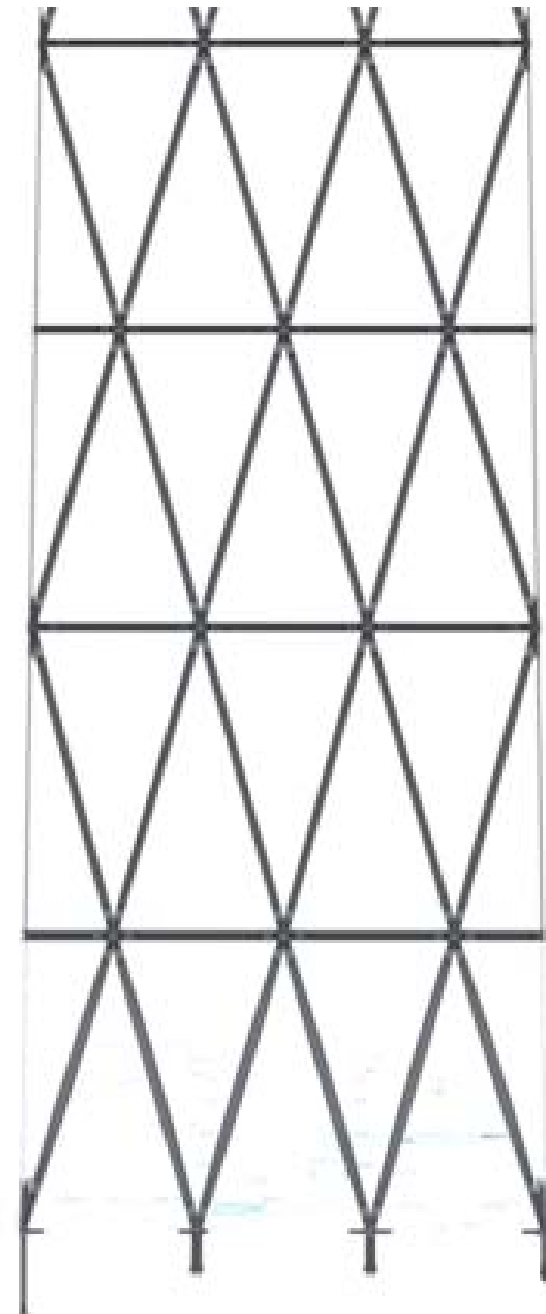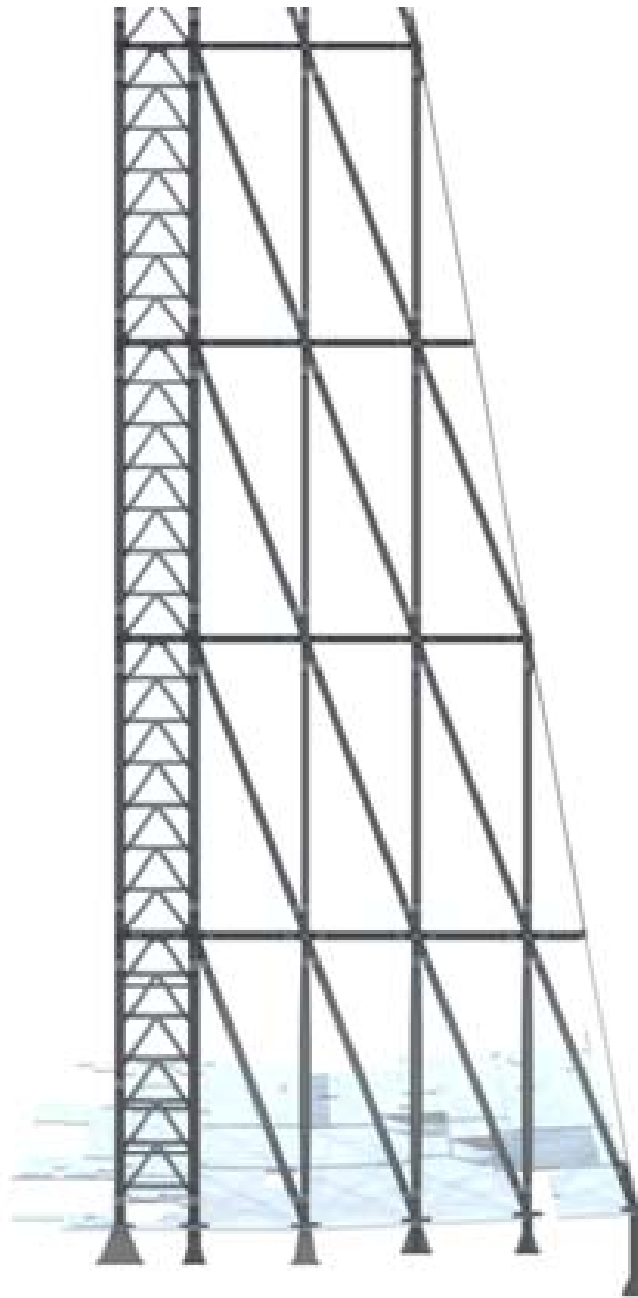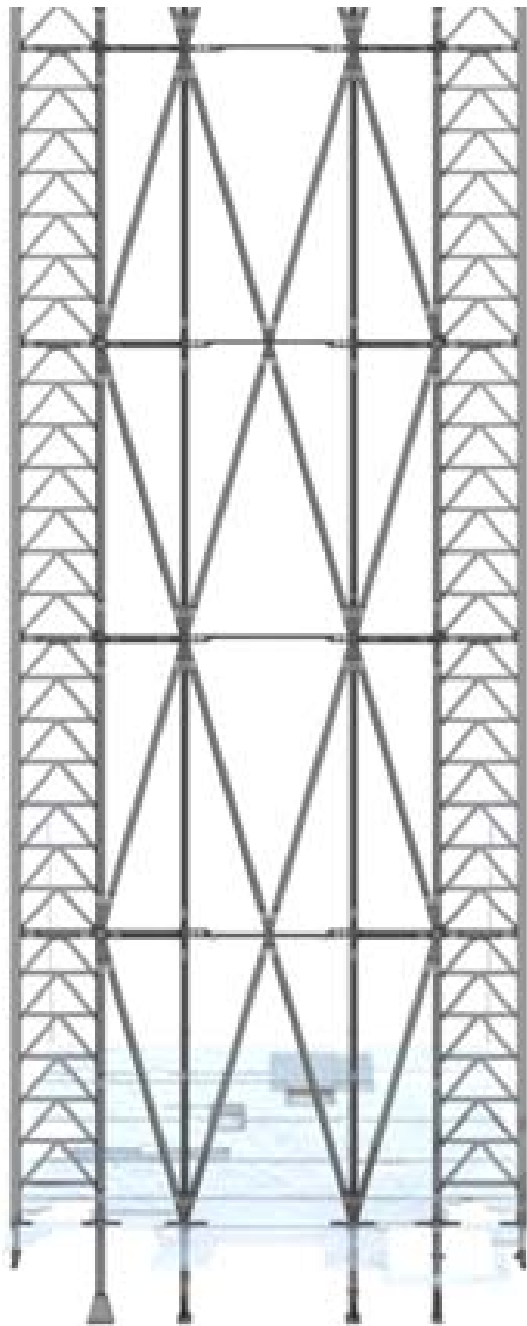



The Megaframe

ARUP

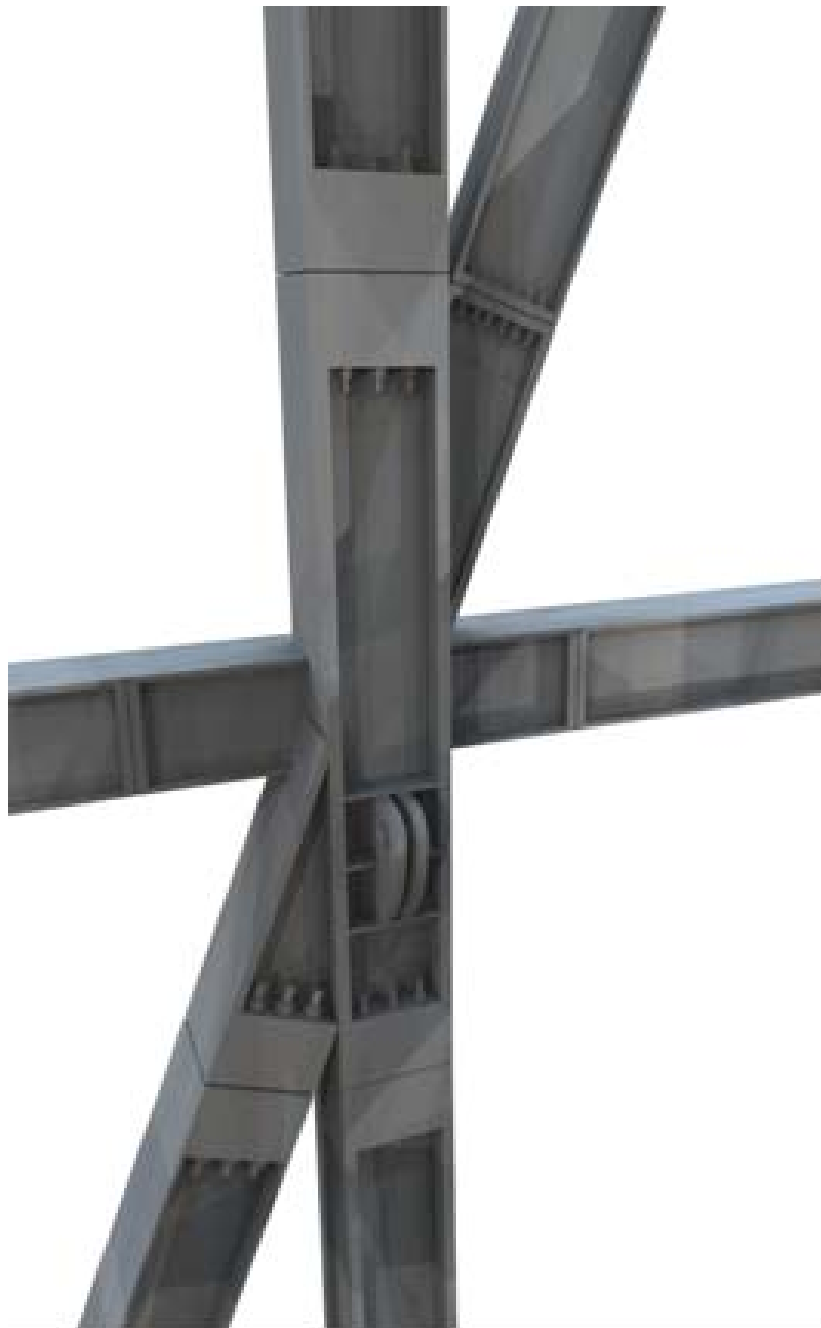


Design for buildability

ARUP

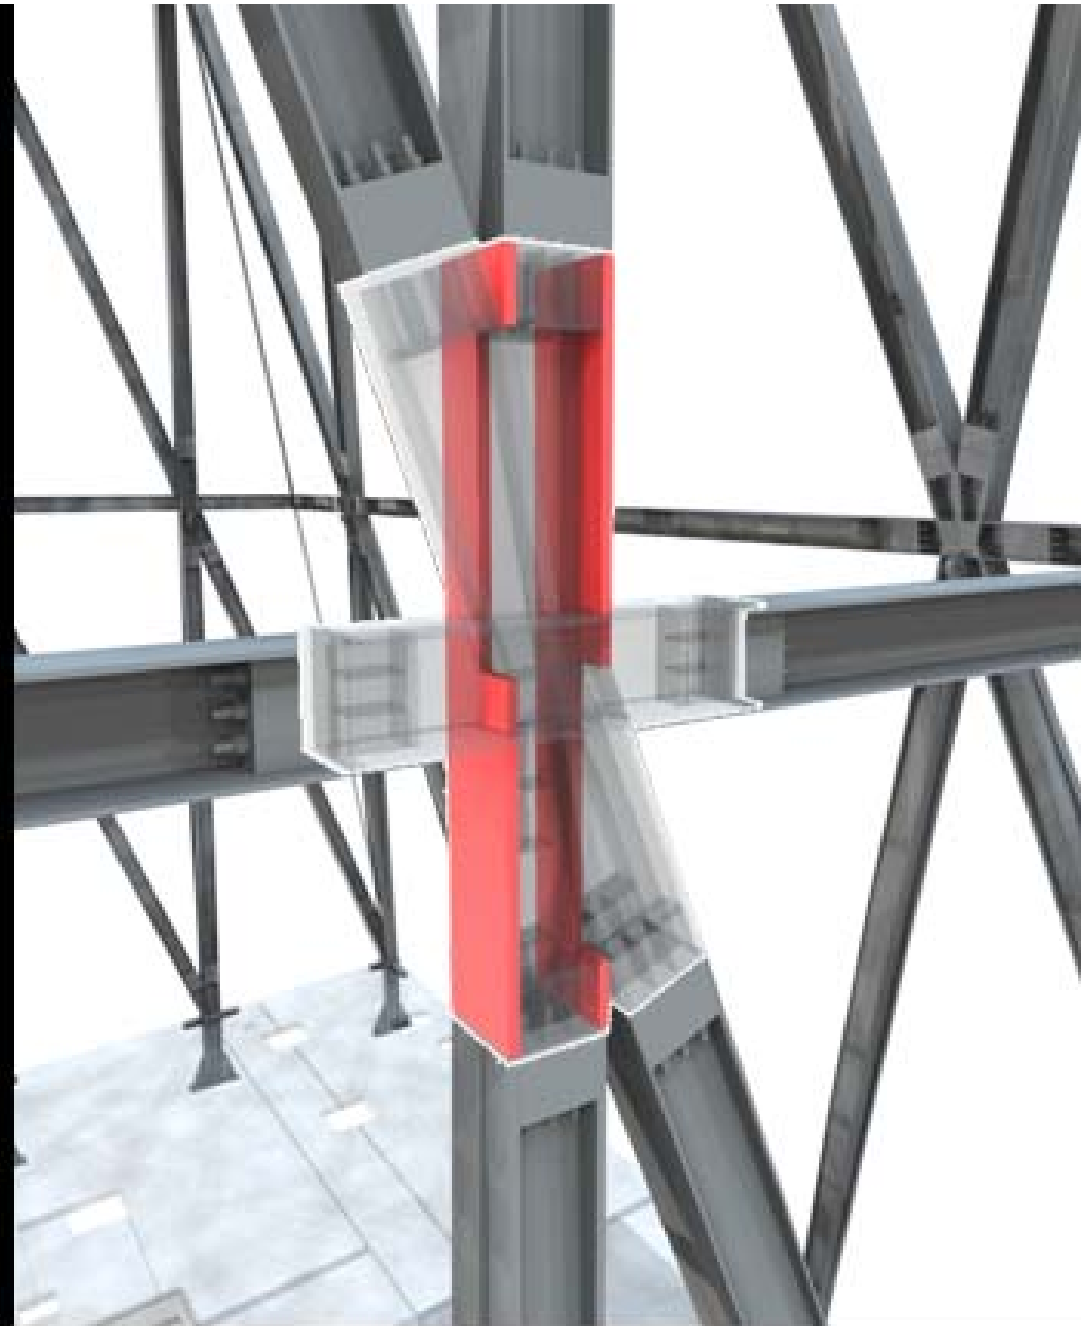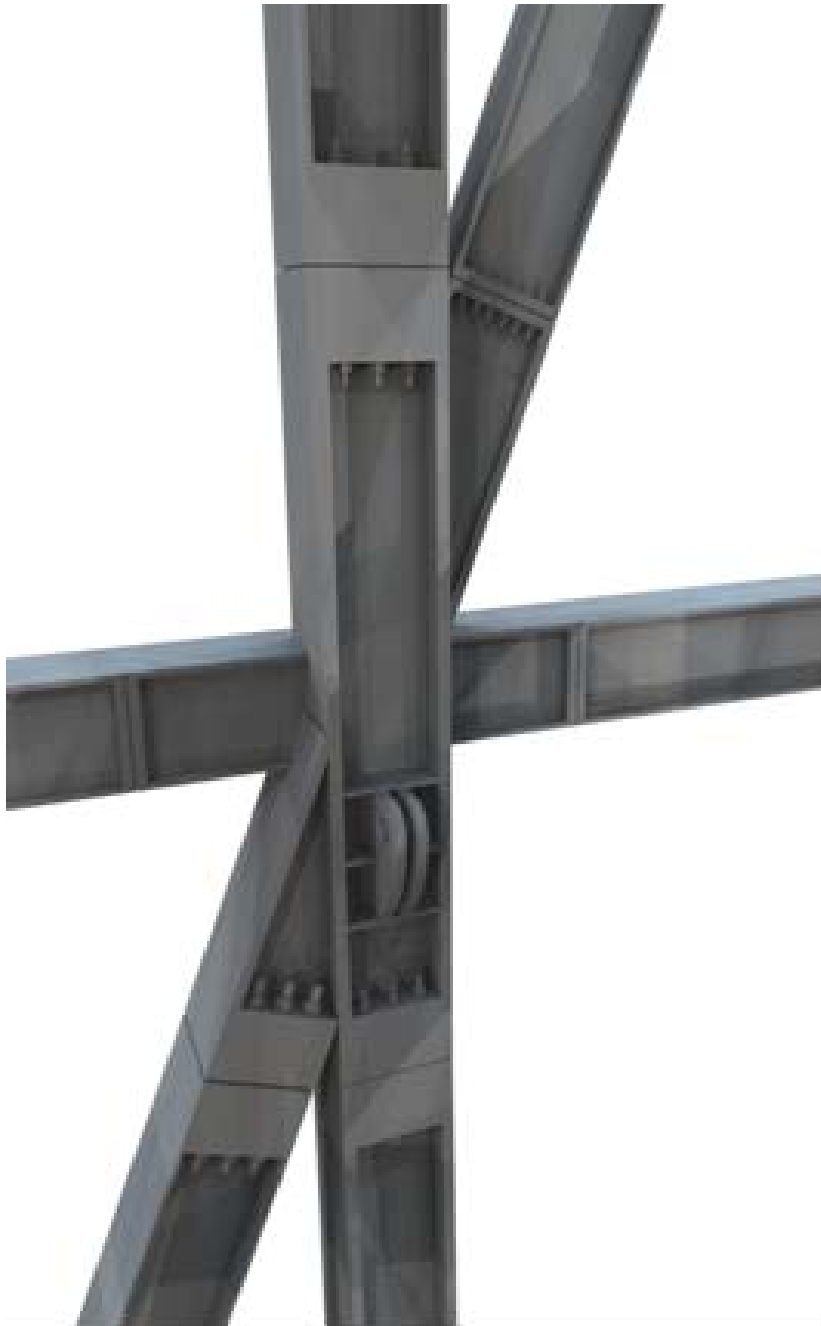


Design for buildability


ARUP

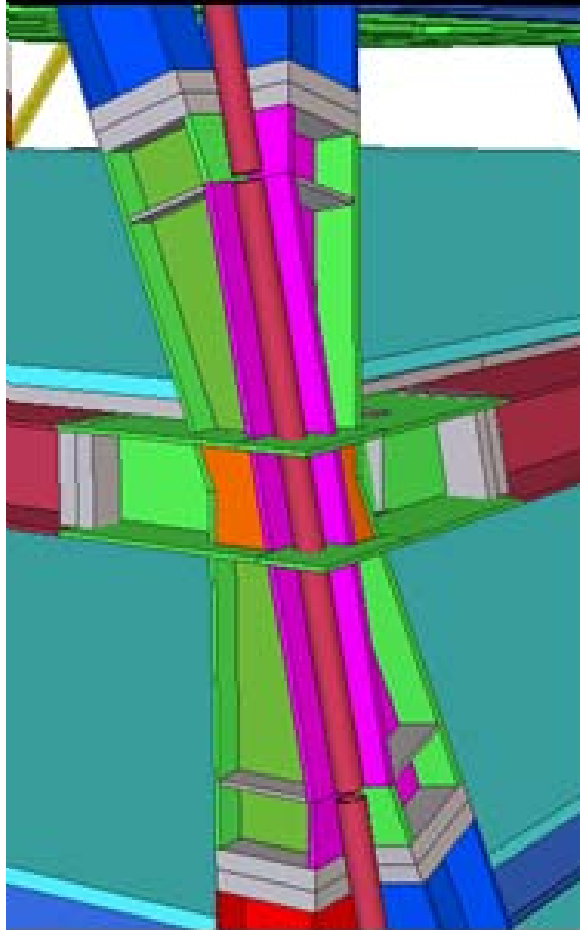

TEKLA

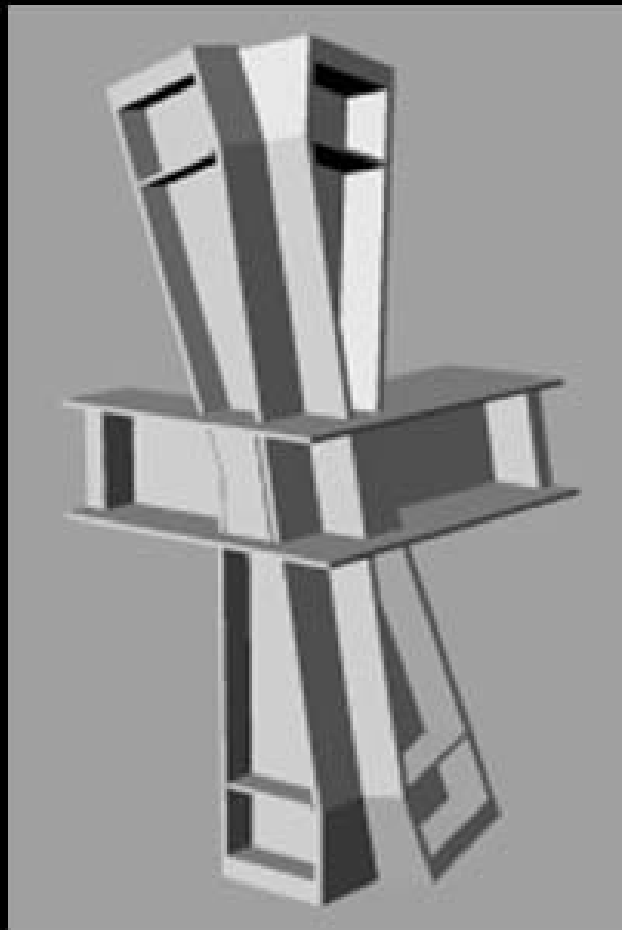

RHINO

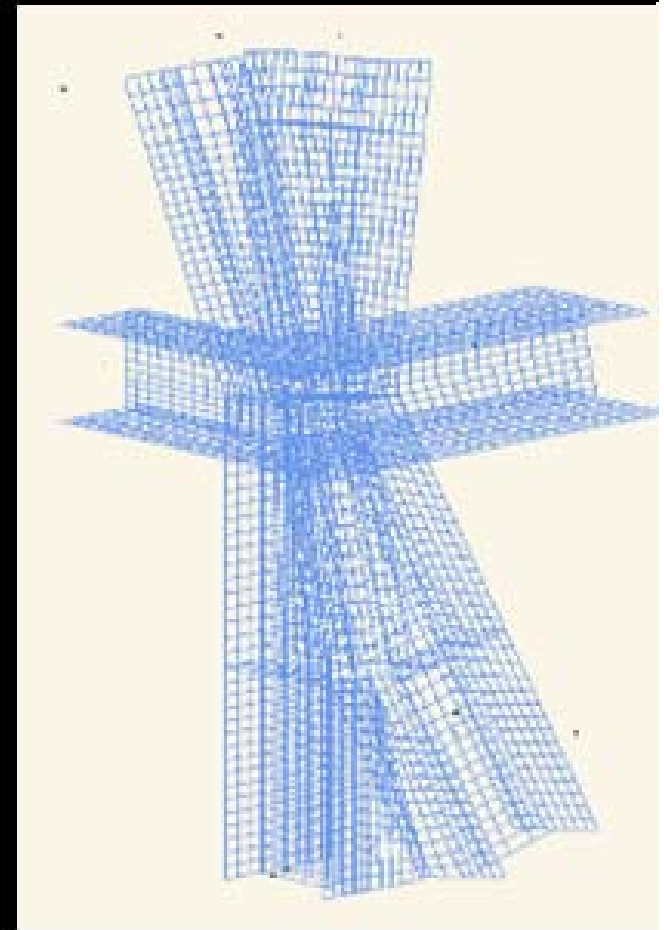


GSA

Modelling, Analysis, Design, Fabrication

ARUP



Analysis, detailing, fabrication

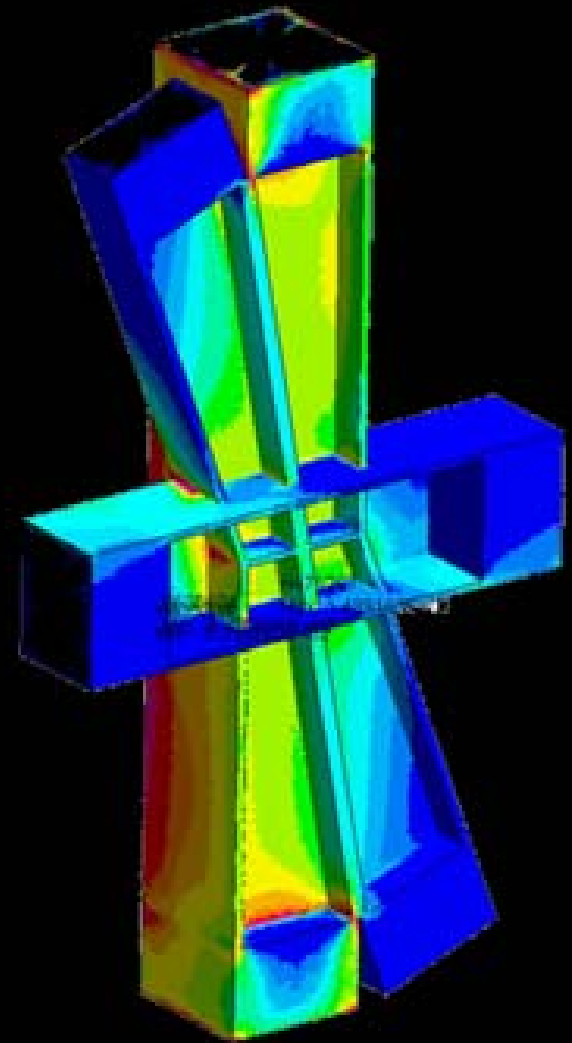

ARUP



Analysis, detailing, fabrication

ARUP




The Leadenhall Building


Building services


James Thonger

ARUP

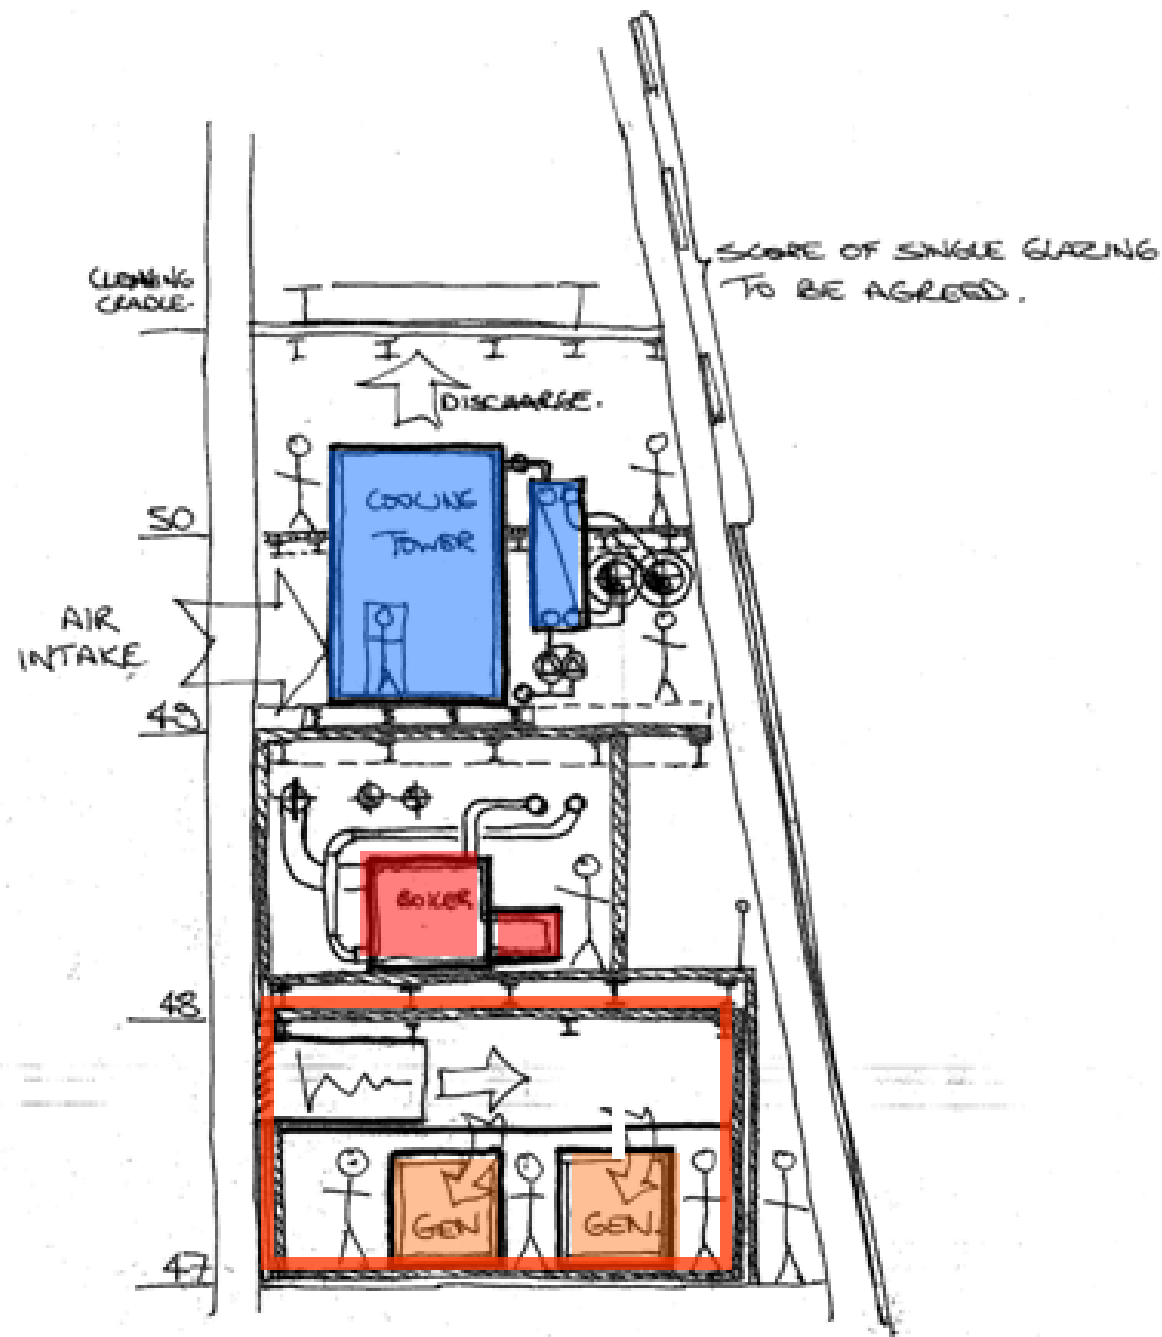



Roof section

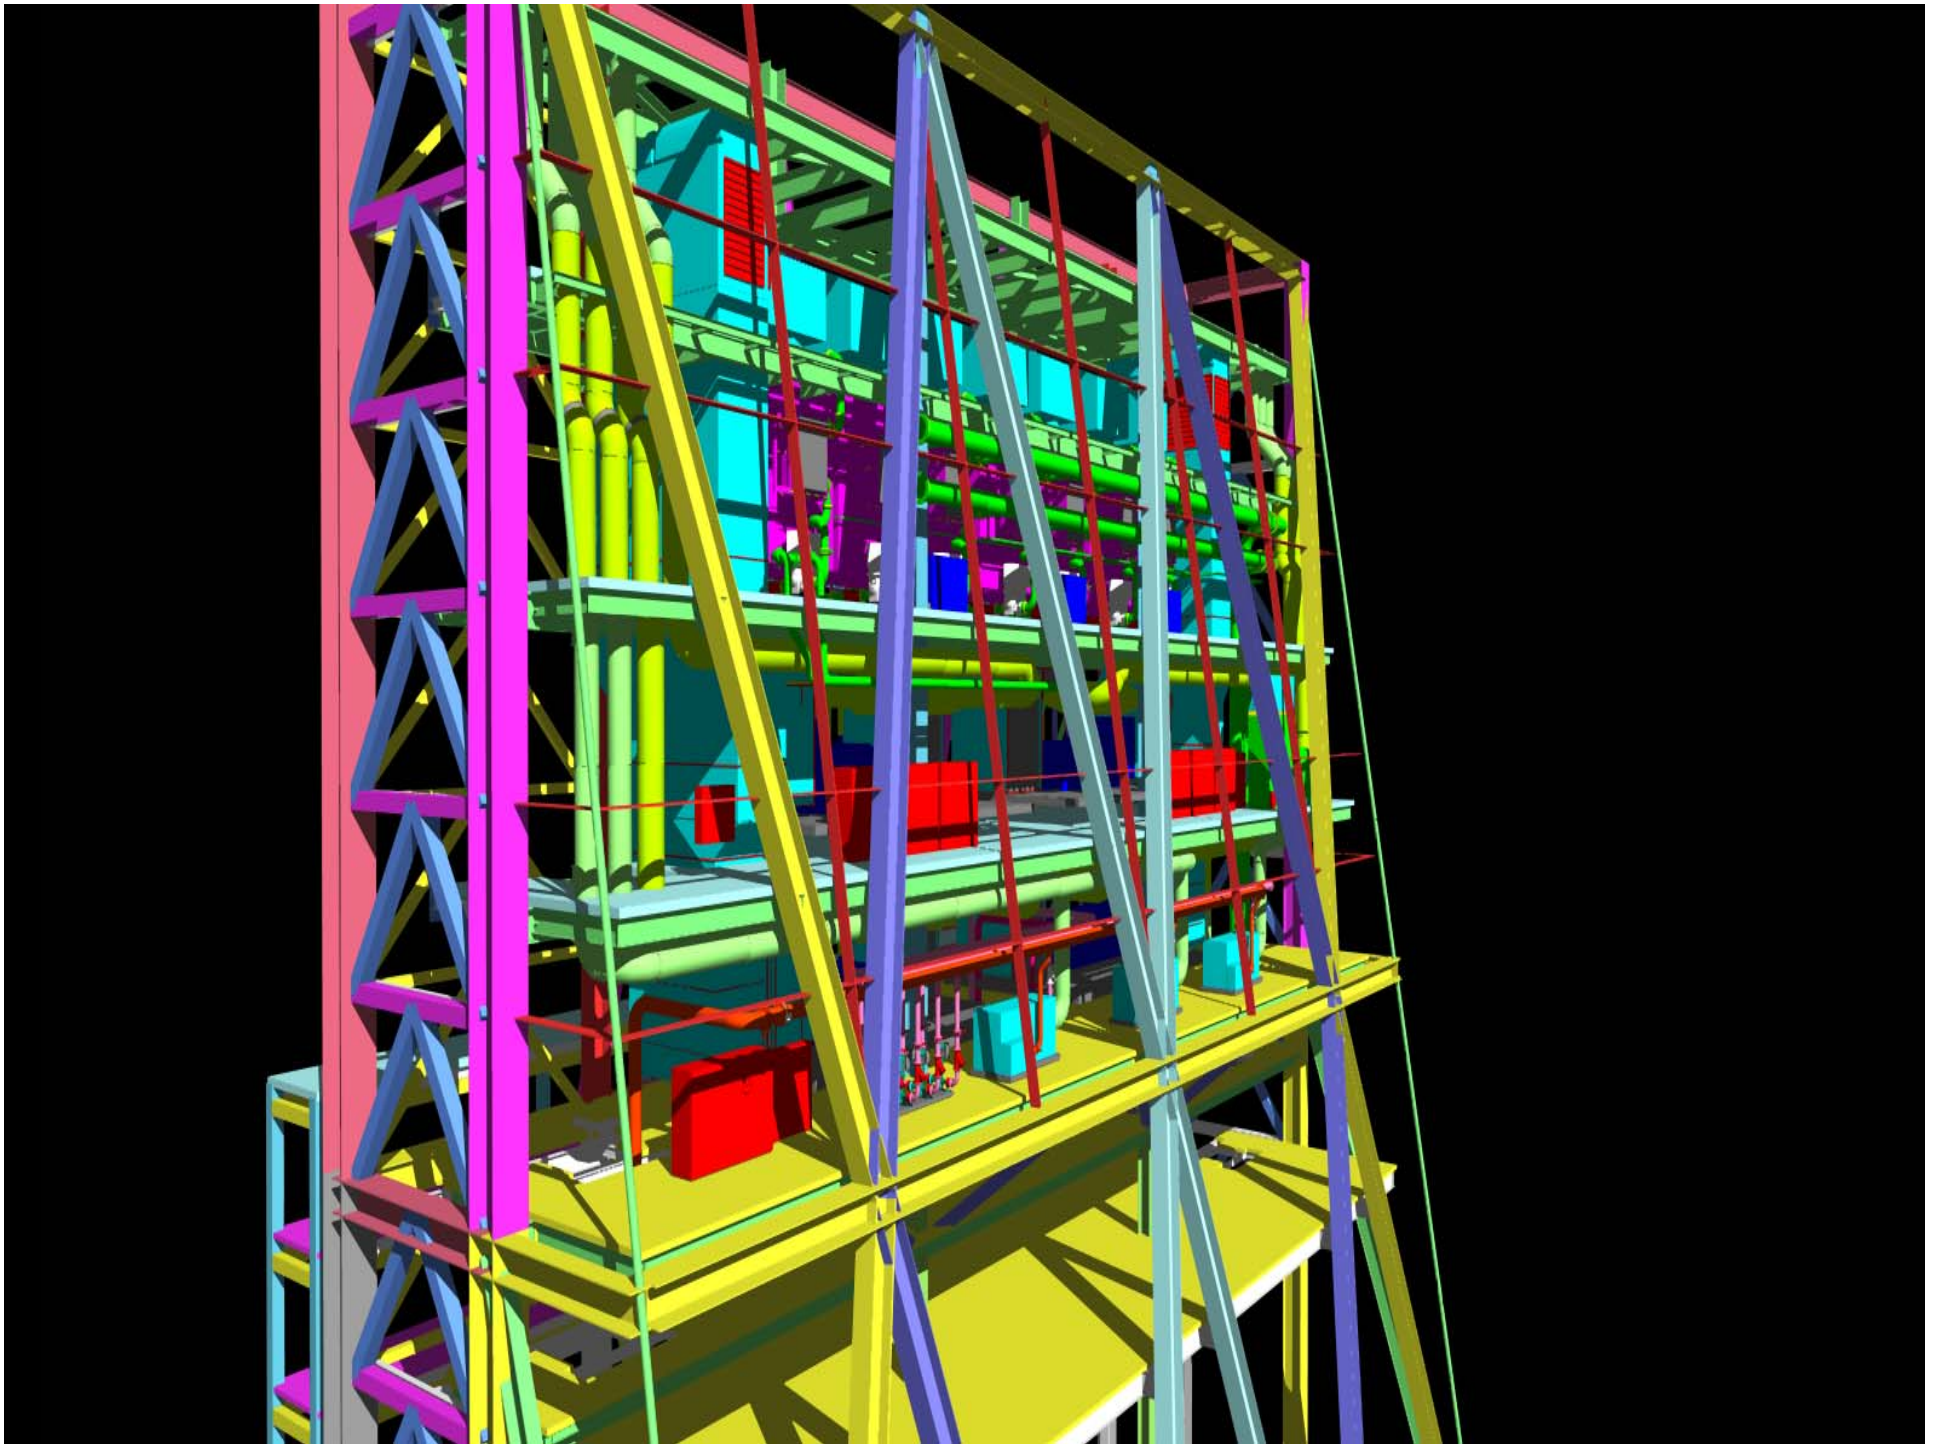

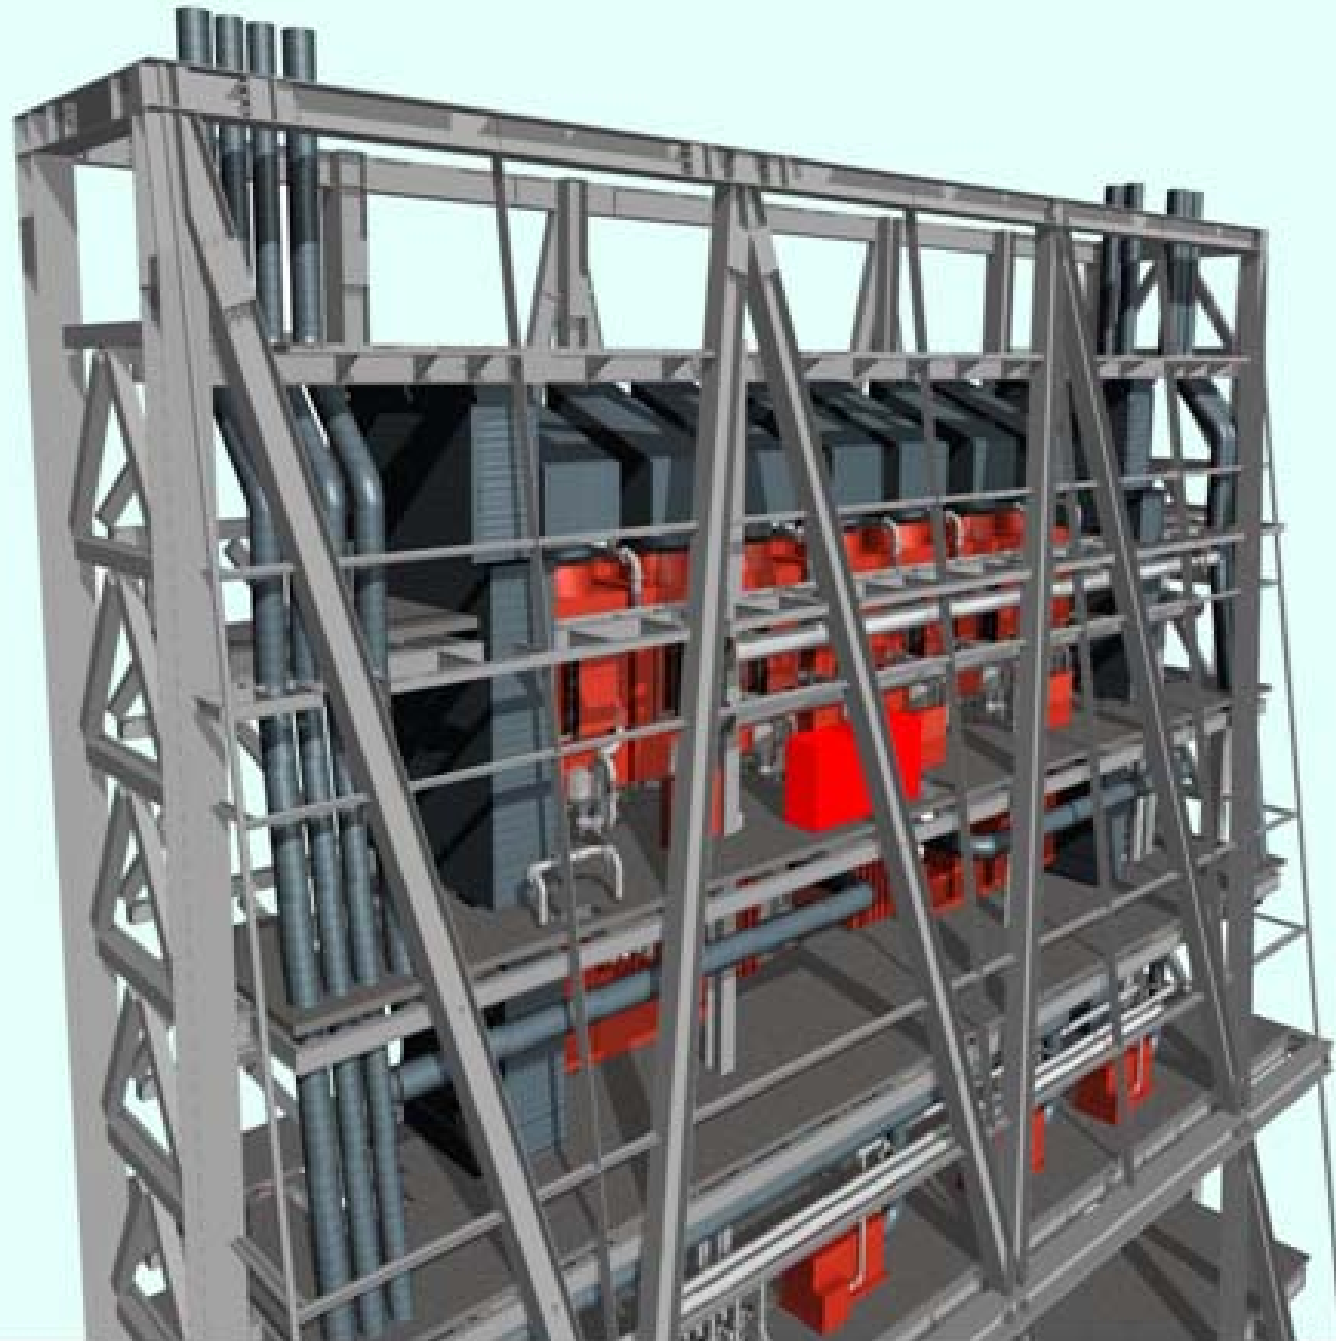


ARUP

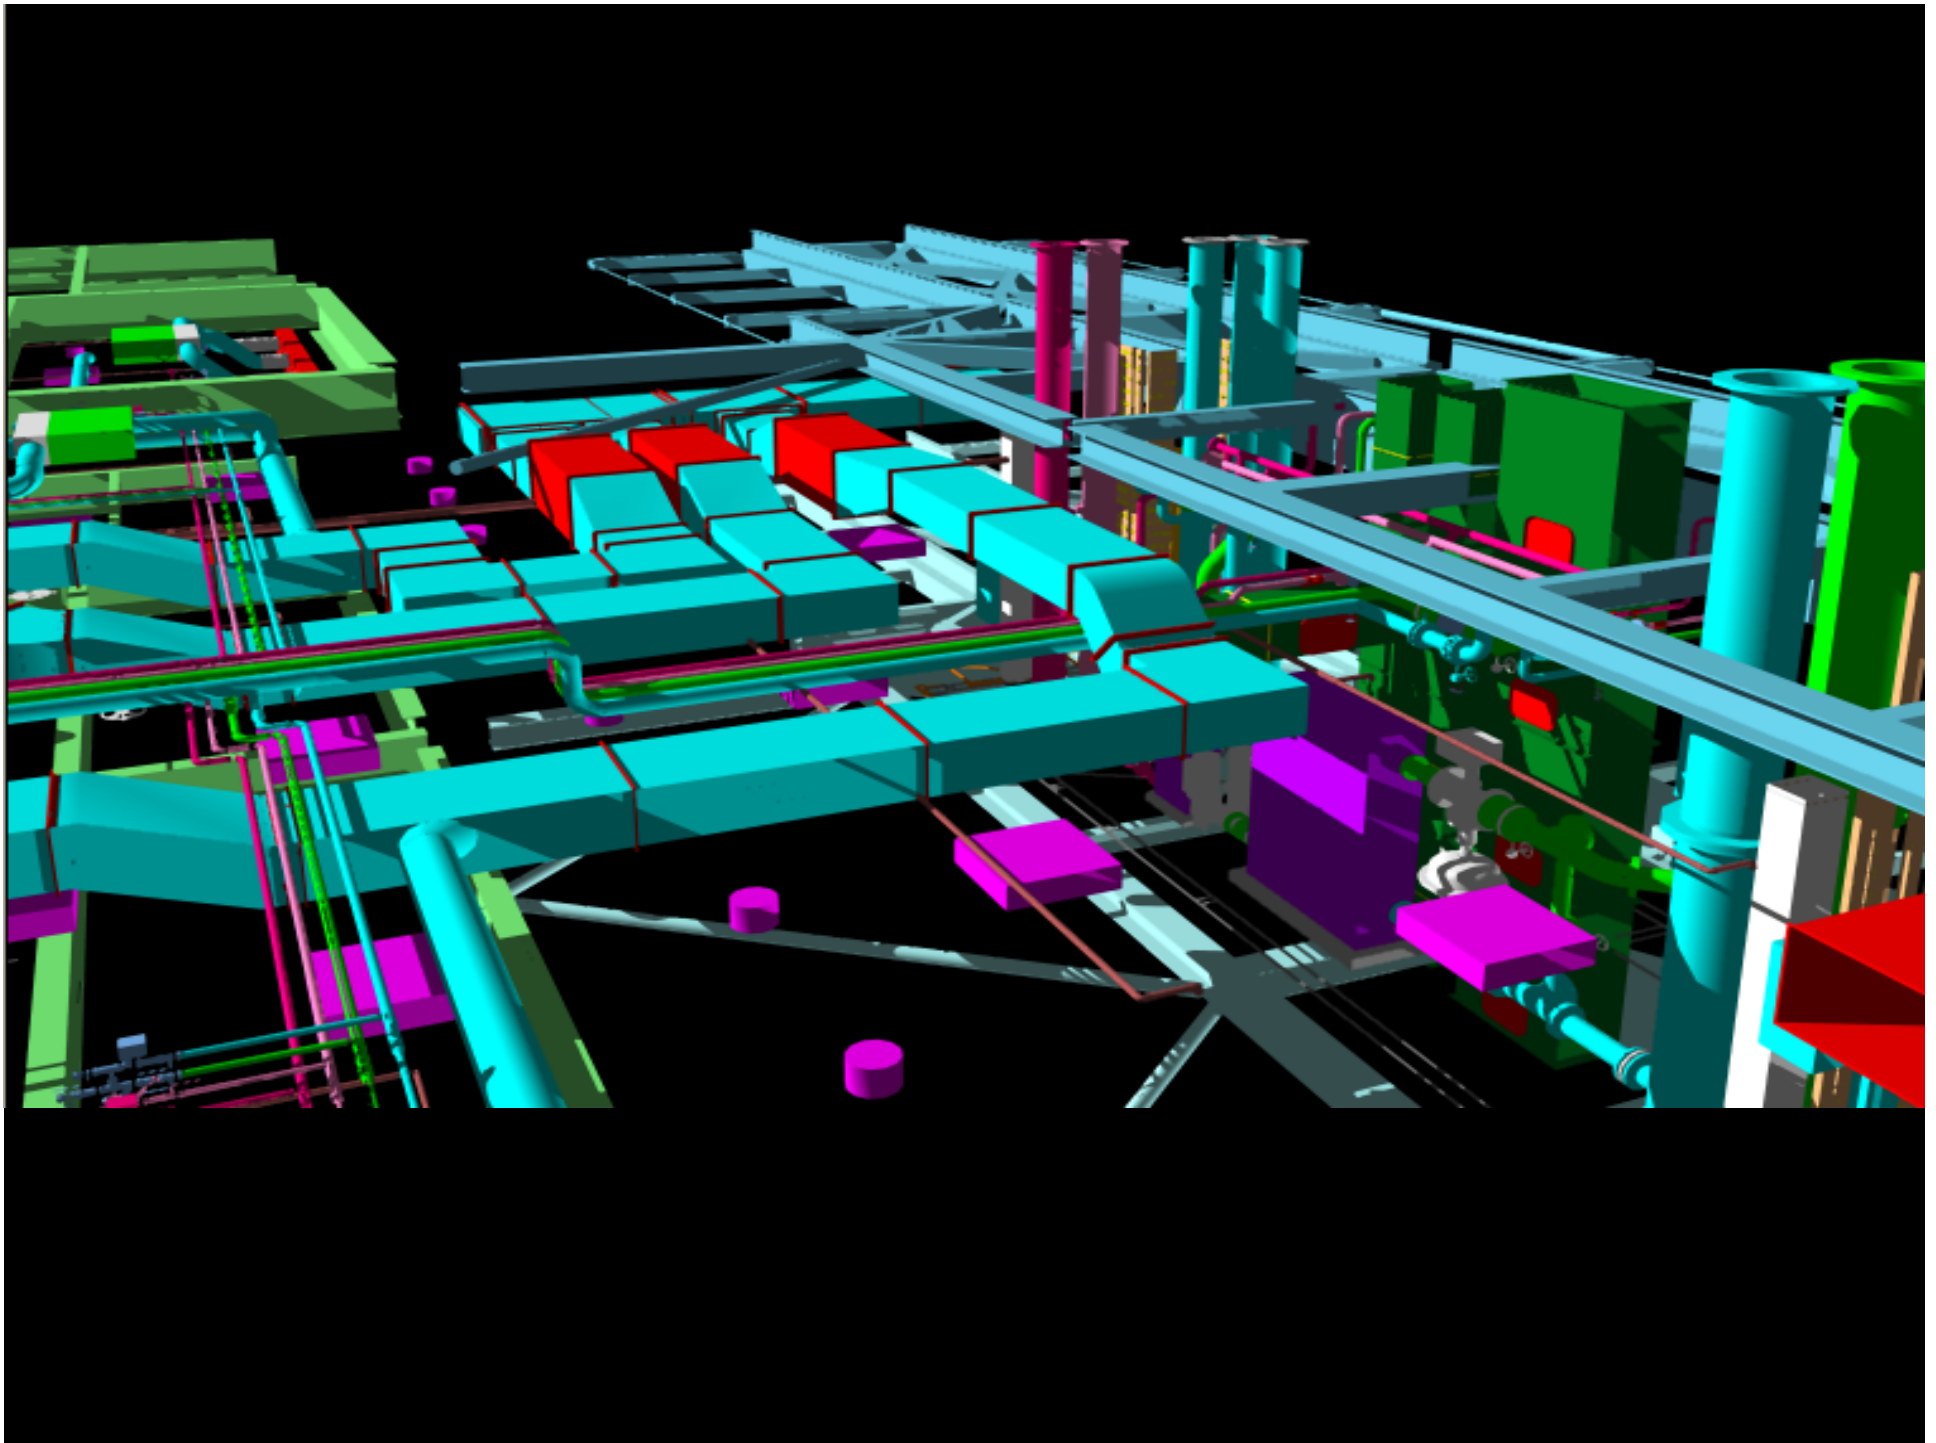

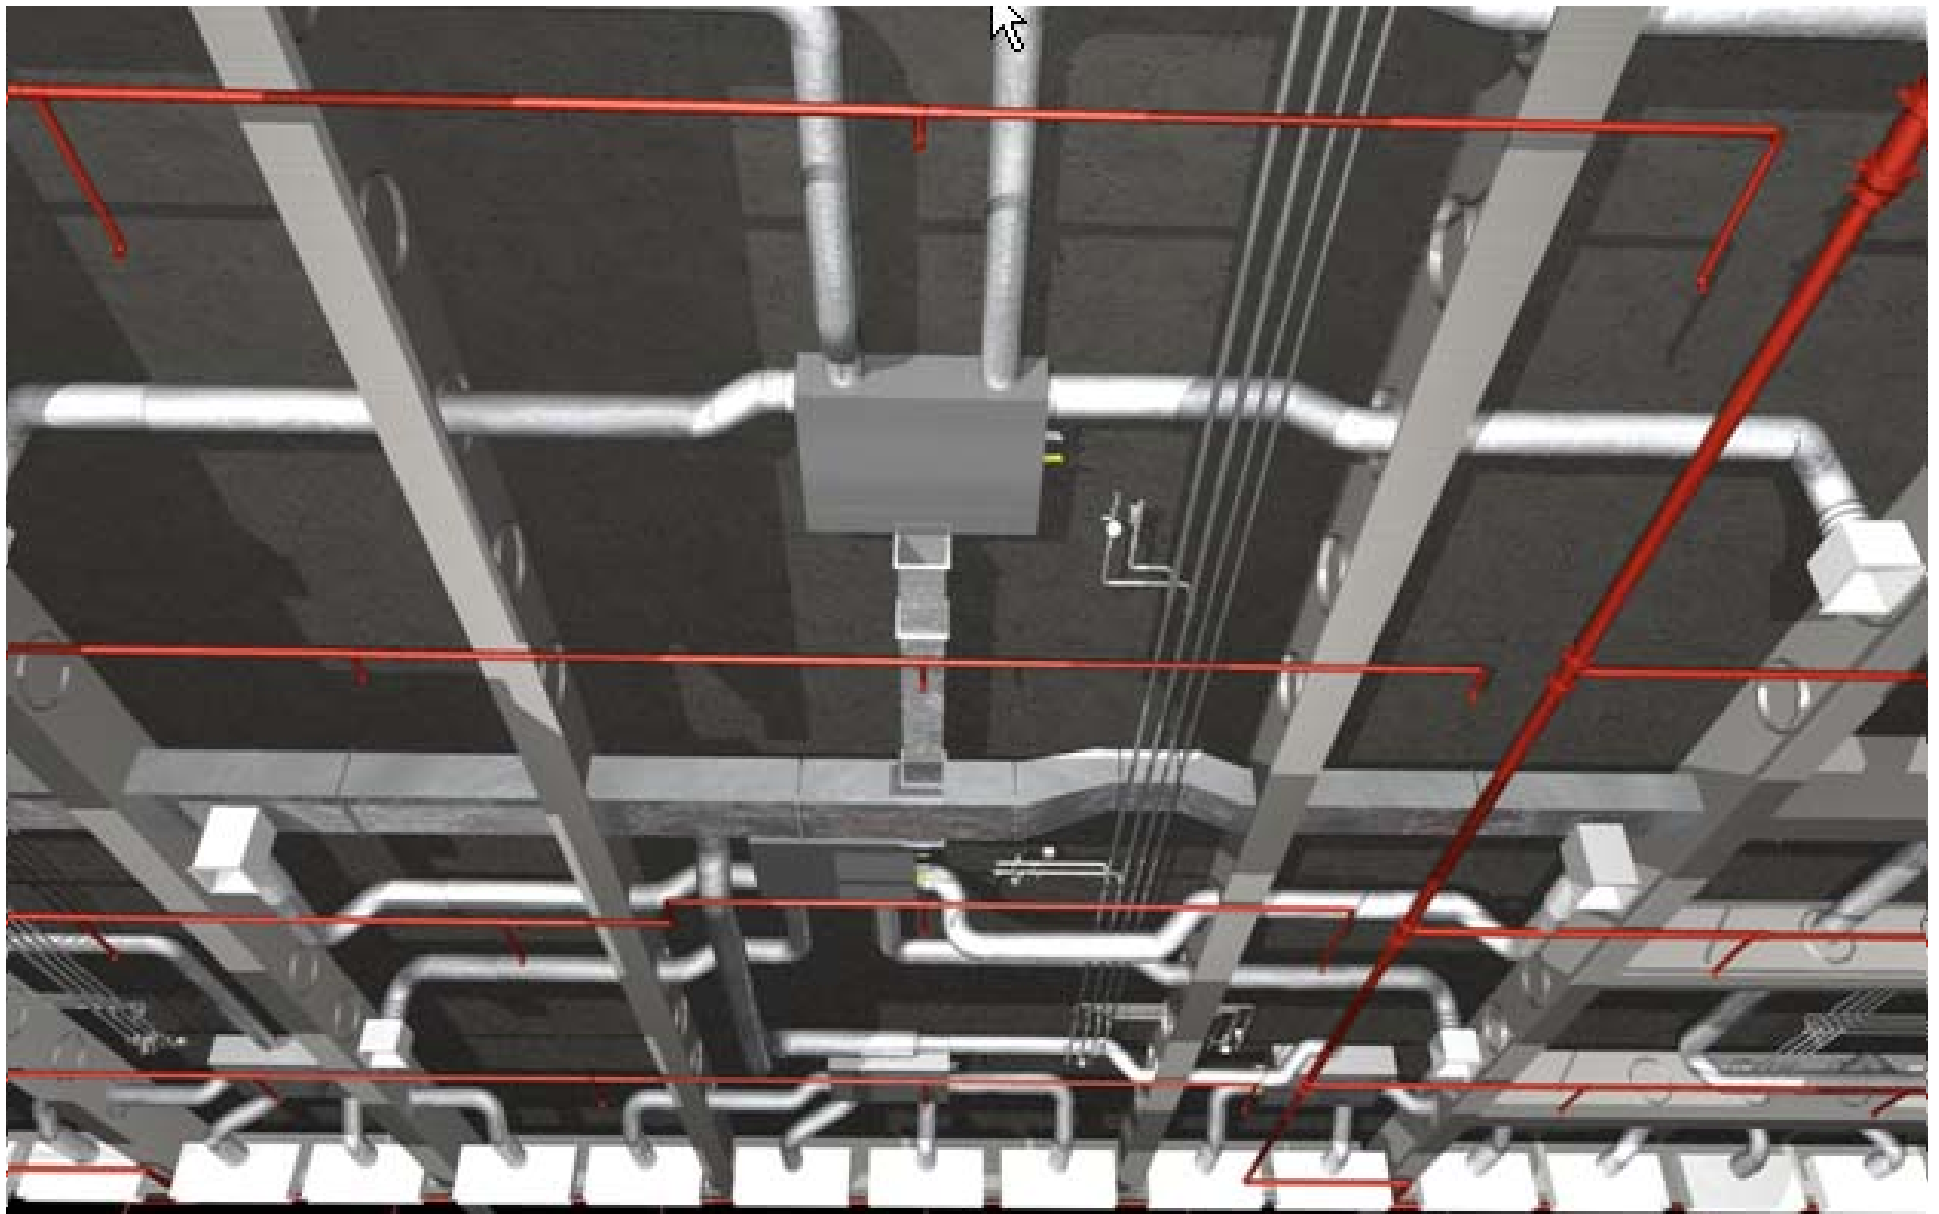

ARUP

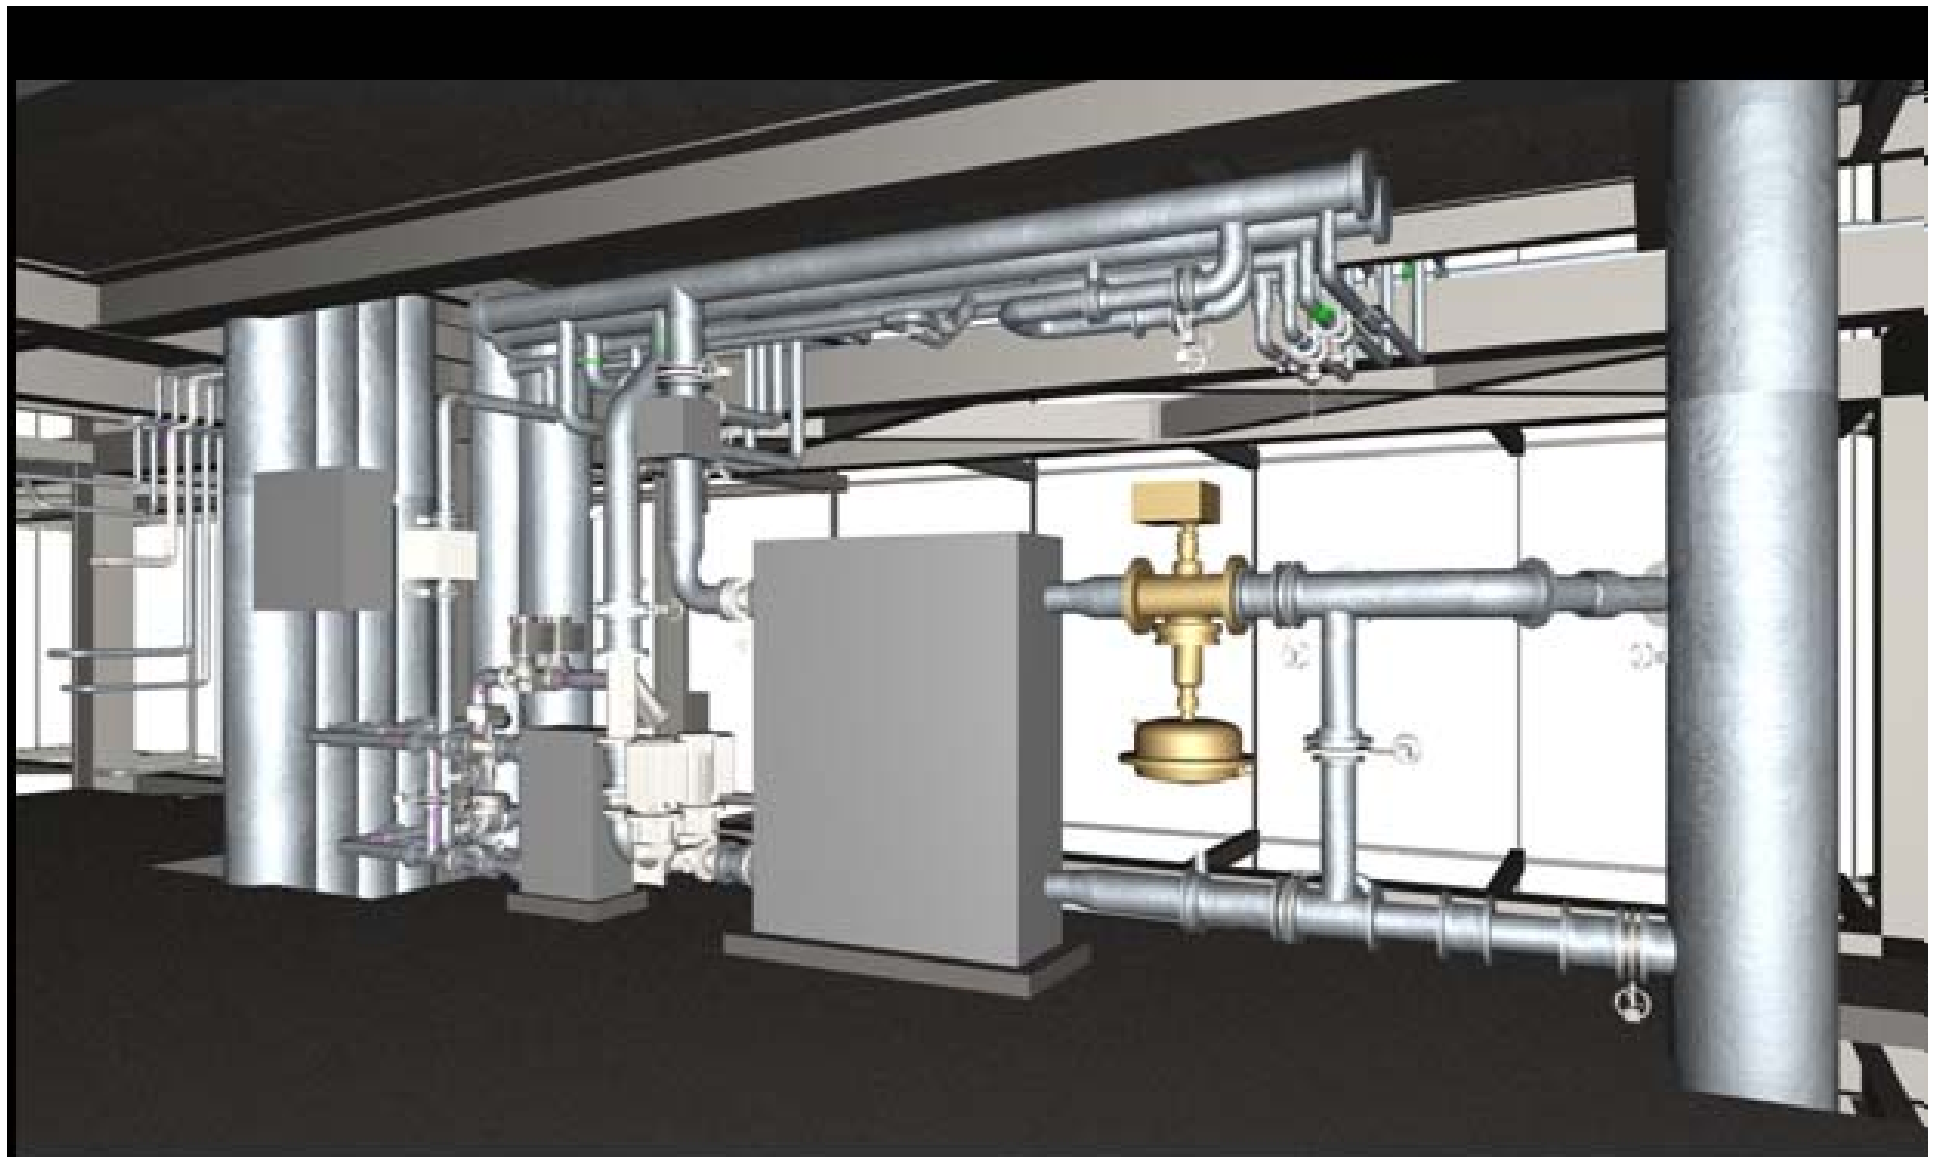

ARUP
